



EXPANSION PROJECT UPDATES

✓ JUNE 8TH, 2026 - **BREAKING GROUND!**



- We've started! (Sometimes it's the hardest part!)
- Primary demolition work is complete!
- Preparing for installation of new water and sanitary sewer piping which will connect in the ALCS parking lot.
- Materials that require a long lead time to manufacture and deliver have been ordered.

✓ JUNE 18TH, 2026 - **UTILITY WORK IN PROGRESS**

- New water and sanitary sewer lines are being installed as part of our building expansion, helping increase the future capacity of City Church

FOR YOUR SAFETY, AND FOR THE MOST EFFICIENT FLOW OF TRAFFIC:

- Please enter and exit on the ALCS (west) side of the building.
- For your safety, do not walk up the hill on the east side of the church.
- When exiting, please use the front doors or sanctuary doors that lead directly outside.

✓ JUNE 25TH, 2026 - **FINISHING UP UTILITY WORK**

- This week we're finishing up the new water and sanitary sewer services which will serve the addition and church. Then we will excavate to prepare for foundations next week.



JULY 2ND, 2026 - FOOTINGS ARE UNDERWAY!



- New water and sanitary sewer utilities have been installed.
- Excavation and footings are underway and will continue next week.



JULY 11TH, 2026 - BUILDING A STRONG FOUNDATION

- Work continues on the concrete foundations for the church addition.




✓ JULY 16TH, 2026 - COMPLETING THE FOUNDATION



- Foundation and backfill should be completed this week!

✓ JULY 23RD, 2026 - THANKS TO OUR HARD WORKING CREW!

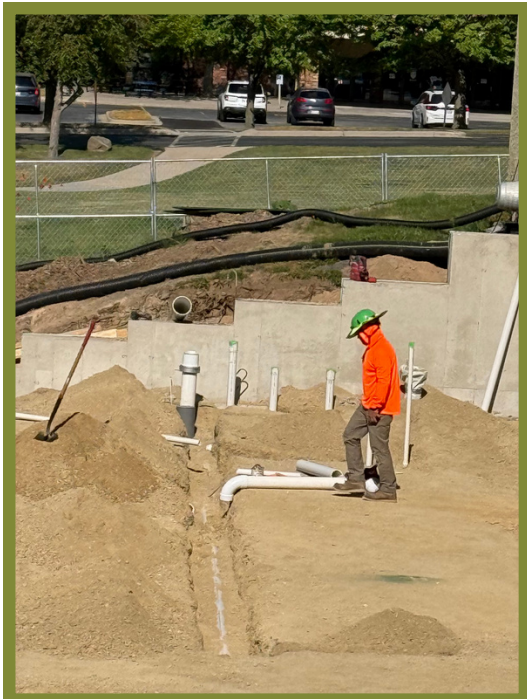

- Foundation and backfill has been completed through intense heat this week! Hats off to our incredibly hard working crew!



JULY 30TH, 2026 - ELEVATOR CONSTRUCTION BEGINS



- Elevator shaft construction is underway. Underground plumbing and electrical work is complete. We are preparing to pour the concrete slab.



AUGUST 6TH, 2026 - STRUCTURAL WORK BEGINS!



- Erecting structural steel is our next step! The concrete floor and the elevator shaft were both completed this week.



AUGUST 13TH, 2026 - THINGS ARE TAKING SHAPE!



- This week will continue with erection and detailing of steel columns, beams, and decking.



AUGUST 20TH, 2026 - FINALIZING STRUCTURAL STEEL



- We are finishing up structural steel and preparing to pour the concrete on the upper floor next week.
